Actual Timeframes | Projected Timeframes
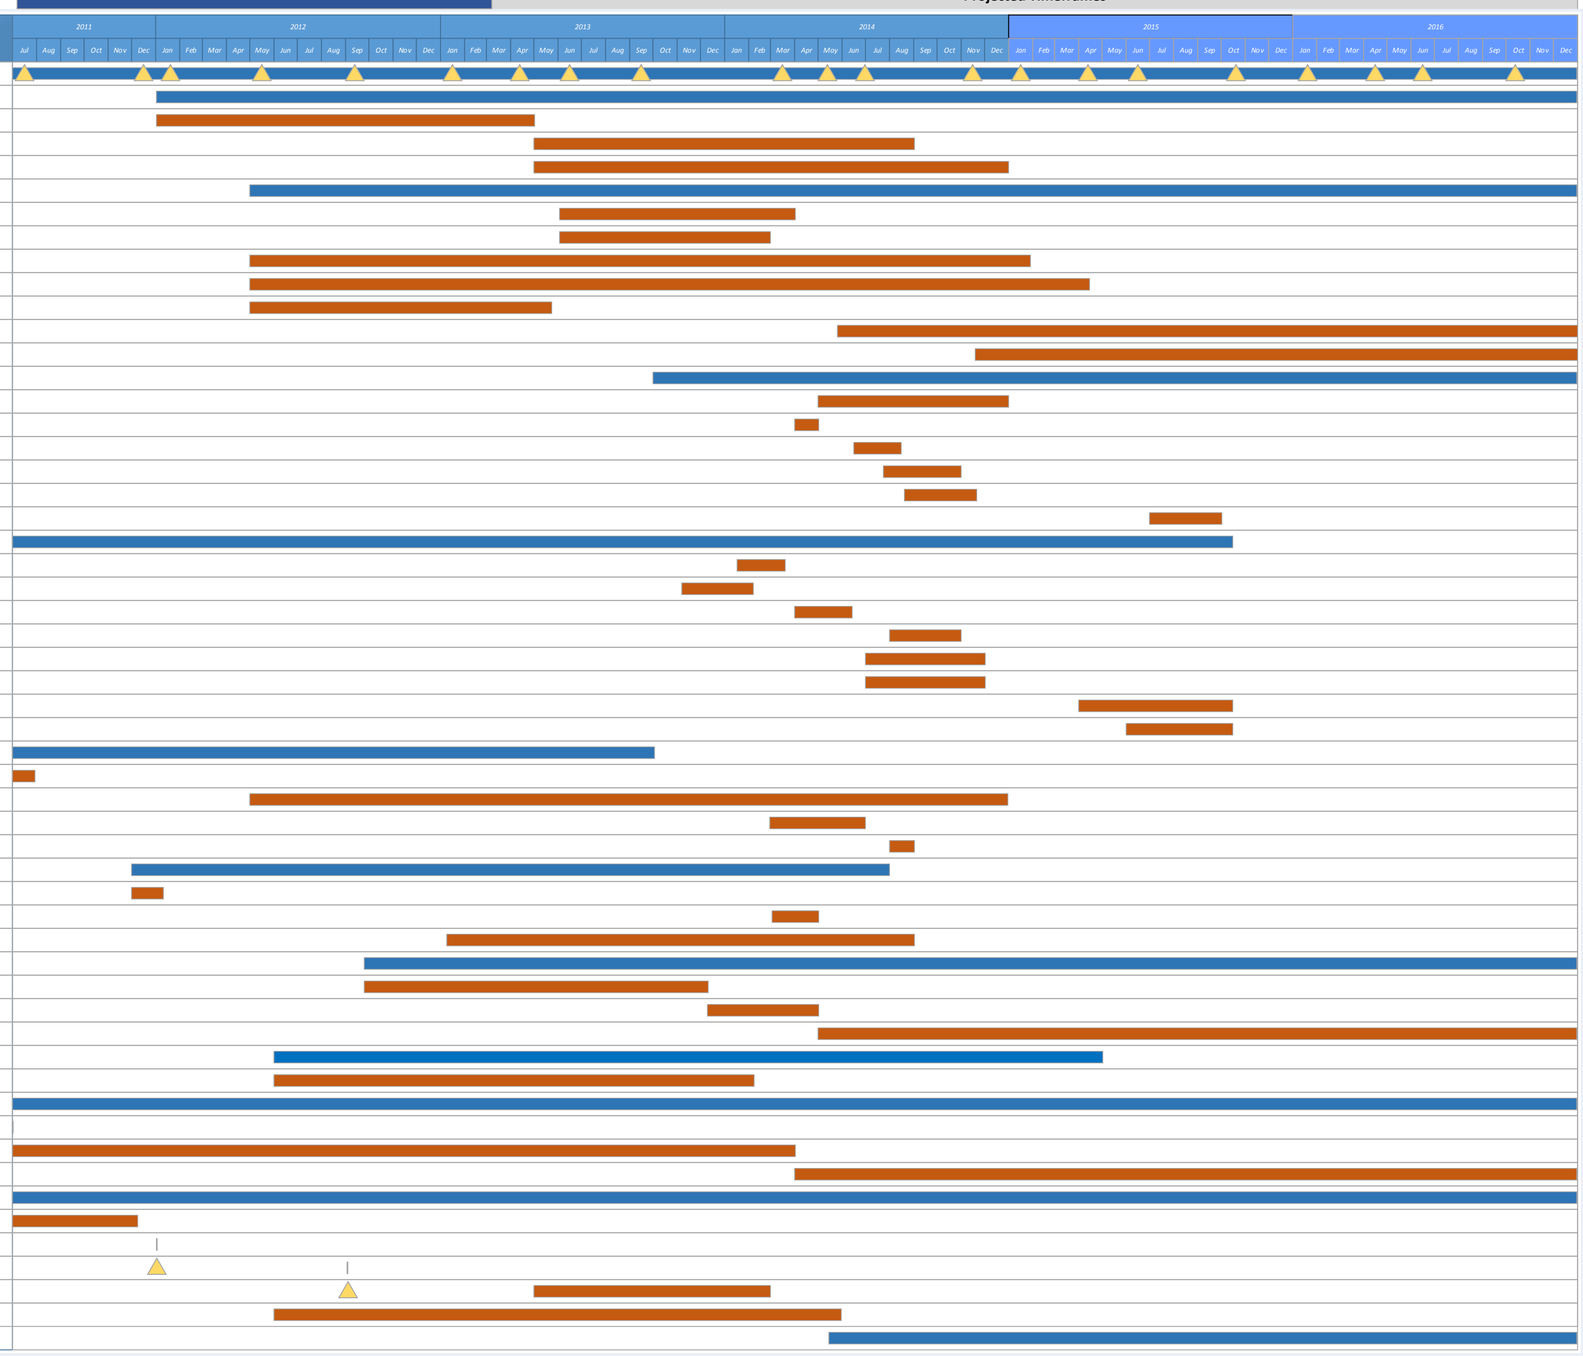
ID	Task Name	Start	Finish
1	CIMI Meetings	7/1/2011	12/30/2016
2	Reference Model	1/2/2012	12/30/2016
3	Reference Model Development	1/2/2012	5/1/2013
4	Revise Reference Model Based on Experience	5/1/2013	9/1/2014
5	Reference Model Maintenance	5/1/2013	12/31/2014
6	Clinical Models	5/1/2012	12/30/2016
7	Agree to Clinical Modeling Patterns	6/3/2013	4/1/2014
8	Define Terminology Binding Syntax	6/3/2013	2/28/2014
9	Develop Laboratory Models	5/1/2012	1/28/2015
10	Develop Patient Measurement Models	5/1/2012	4/14/2015
11	Develop Order Models	5/1/2012	5/23/2013
12	Develop Immunization Models	5/26/2014	10/12/2017
13	Develop Genetic Models	11/19/2014	2/18/2019
14	Model Repository	10/1/2013	12/30/2016
15	Make Models Available in NCBO Repository	5/1/2014	12/31/2014
16	Load Laboratory Models	4/1/2014	5/1/2014
17	Load Patient Measurement Models	6/16/2014	8/15/2014
18	Load Order Models	7/24/2014	10/31/2014
19	Load Immunization Models	8/20/2014	11/20/2014
20	Load Genetic Models	7/1/2015	10/1/2015
21	Tooling	7/1/2011	10/15/2015
22	Create Compiler for Conversion of CEML to ADL	1/17/2014	3/19/2014
23	Enhance Compiler to Convert CEML to FHIR Profiles	11/7/2013	2/6/2014
24	Enhance Compiler to Convert ADL to FHIR Profiles	4/1/2014	6/13/2014
25	Enhance Compiler to Produce RDF and ADL	8/1/2014	10/31/2014
26	Enhance Compiler to Produce AML from ADL	7/1/2014	12/1/2014
27	Integrate Models With Data Entry Screen Authoring	7/1/2014	12/1/2014
28	Integrate Models With CDS Authoring	4/1/2015	10/15/2015
29	Integrate Models With Quality Measure Authoring	6/1/2015	10/15/2015
30	UML Representation	7/1/2011	10/2/2013
31	Submit Project to OMG	7/1/2011	7/29/2011
32	Develop Draft Representation	5/1/2012	12/30/2014
33	Respond to Comments	2/28/2014	6/30/2014
34	OMG Approval	8/1/2014	9/1/2014
35	Terminology	12/1/2011	7/31/2014
36	Select Preferred Terminologies	12/1/2011	1/10/2012
37	Select Medication Terminology	3/3/2014	5/1/2014
38	Establish Terminology Authority	1/9/2013	9/1/2014
39	Library Management Board	9/25/2012	12/30/2016
40	Develop Policy	9/25/2012	12/10/2013
41	Approve Policy	12/10/2013	5/1/2014
42	Operate Library Management Board	5/1/2014	12/30/2016
43	Licensing Agreements	6/1/2012	5/1/2015
44	IHTSDO	6/1/2012	2/7/2014
45	Website	7/1/2011	12/30/2016
46	Establish Wiki	7/1/2011	7/1/2011
47	Stand Up Website	7/1/2011	4/1/2014
48	Maintain Website	4/1/2014	12/30/2016
49	Governance	7/1/2011	12/30/2016
50	Define Goals and Principles	7/1/2011	12/8/2011
51	Establish Interim Executive Committee	1/2/2012	1/2/2012
52	Establish Permanent Executive Committee	9/3/2012	9/3/2012
53	Define Membership Policies	5/1/2013	2/28/2014
54	Contract for Administrative Support	6/1/2012	5/30/2014
	Publications on CIMI Methods and Experiences	5/15/2014	12/30/2016
